UCRL-17932

cy. 2

# University of California

# Ernest O. Lawrence Radiation Laboratory

BEVATRON OPERATION AND DEVELOPMENT. 55

July through September 1967

Kenneth C. Crebbin and Robert Frias

January 31, 1968

TWO-WEEK LOAN COPY

*This is a Library Circulating Copy which may be borrowed for two weeks. For a personal retention copy, call Tech. Info. Division, Ext. 5545*

UCRL-17932 cy. 2

I

## DISCLAIMER

This document was prepared as an account of work sponsored by the United States Government. While this document is believed to contain correct information, neither the United States Government nor any agency thereof, nor the Regents of the University of California, nor any of their employees, makes any warranty, express or implied, or assumes any legal responsibility for the accuracy, completeness, or usefulness of any information, apparatus, product, or process disclosed, or represents that its use would not infringe privately owned rights. Reference herein to any specific commercial product, process, or service by its trade name, trademark, manufacturer, or otherwise, does not necessarily constitute or imply its endorsement, recommendation, or favoring by the United States Government or any agency thereof, or the Regents of the University of California. The views and opinions of authors expressed herein do not necessarily state or reflect those of the United States Government or any agency thereof or the Regents of the University of California.

UCRL-17932
UC-28 Particle Accel. and
High Volt. Mach.
TID-4500 (51st Ed.)

UNIVERSITY OF CALIFORNIA

Lawrence Radiation Laboratory
Berkeley, California

AEC Contract No. W-7405-eng-48

# BEVATRON OPERATION AND DEVELOPMENT. 55

July through September 1967

Kenneth C. Crebbin and Robert Frias

January 31, 1968

Printed in the United States of America
Available from
Clearinghouse for Federal Scientific and Technical Information
National Bureau of Standards, U. S. Department of Commerce
Springfield, Virginia 22151
Price: Printed Copy $3.00; Microfiche $0.65

# BEVATRON OPERATION AND DEVELOPMENT. 55

July through September 1967

## Contents

Abstract . . . . . iv
I. Machine Operation and Experimental Program . . . . . 1
II. Shutdown . . . . . 7
III. Bevatron Development and Studies . . . . . 7
IV. Magnet Power Supply
A. Failure of a Generator Field Pole Connection . . . . . 8
B. Stability of the Flat-Top Current Slope . . . . . 11
Staff . . . . . 14

*Preceding Quarterly Reports: UCRL-17931, UCRL-17543.

# BEVATRON OPERATION AND DEVELOPMENT. 55

July through September 1967

Kenneth C. Crebbin and Robert Frias

Lawrence Radiation Laboratory
University of California
Berkeley, California

January 31, 1968

## ABSTRACT

The beam was off 5.8% of the scheduled operating time because of equipment failure and 5.8% of the time for experimental setup, tuning, and routine checks. The beam was on for 88.4% of the scheduled operating time. During this quarter, the Bevatron accelerated $2.05 \times 10^{18}$ protons.

The maximum operating beam intensity was raised to $4 \times 10^{12}$ protons per pulse.

Construction on the new External Proton Beam Hall and new two-channel beam facility continued. An experiment was set up at the second focus in channel I, and preliminary tests were made on the new beam transport system to that area.

Tests continued on the resonant extraction system for the external proton beam.

A generator field pole connection on one of the main motor generator sets failed on September 24. The Bevatron was shut down for about 2 weeks to rebraze all the field pole connections on both motor generator sets.

# I. MACHINE OPERATION AND EXPERIMENTAL PROGRAM

The Bevatron operation record is shown in Fig. 1. The beam was off 5.8% of the scheduled operating time because of equipment failure and 5.8% of the time for experimental setup, tuning, and routine checks. The beam was on for 88.4% of the scheduled operating time. During this quarter, the Bevatron accelerated $2.05 \times 10^{18}$ protons.

When we resumed operation in June 1967, the maximum allowed operating intensity was raised from $3 \times 10^{12}$ to $4 \times 10^{12}$ protons per pulse. The maximum that we achieved, however, during the first 2 months of operation, was $3.5 \times 10^{12}$ protons per pulse, and we generally operated between 2.5 to $3 \times 10^{12}$ protons per pulse. In the middle of July the operations crews were encouraged to try to increase the beam intensity to the new maximum allowed operating level. On August 4 the crew reached an operating intensity of $4 \times 10^{12}$ protons per pulse and were able to operate at this intensity level whenever the experiments could use the full beam.

Construction continued through this quarter on the new External Proton Beam (EPB) Hall. Excavations were made for the utility tunnels during July. The tunnels were formed and poured during August and September. The layout is shown in Fig. 2. The new curved-bridge crane was installed in the new EPB Hall (see Fig. 3). Final testing of this crane was under way at the end of the quarter, and final acceptance is hoped for at an early date, so the crane can be used for the installation of the EPB shielding in the backstop area.

The Lofgren Group Experiment 67 was set up at the second focus in EPB channel I. A temporary backstop was installed between the second and third focus to allow running beam for tune-up and operation of this experiment. It also permited checking the operation of the EPB channel up to the second focus (F 2). (See Fig. 2.)

There were two basic modes of magnet pulsing this quarter. The first mode was a 300-msec flat-top at 6.1 BeV. In this mode the 25-inch bubble chamber and the University of Washington—U. C. San Diego Group (Williams, Masek; Expt. 50) ran on alternate magnet pulses. The 25-inch Bubble Chamber Group received a 300-μsec beam spill just after the start of flat-top and a second 300-μsec spill just before the end of flat-top. On the alternate pulse the University of Washington Group received a 150-msec spill during the flat-top. (See Fig. 4.) The University of Washington (Davis) Group (Expt. 54) was set up downstream from the University of Washington—U. C. San Diego (Expt. 50) secondary beam-channel target and detectors.

The second mode of magnet pulsing was a 900-msec flat-top at 5.3 BeV. The Moyer Group received a 600- to 800-msec spill during this period (Fig. 4b). The Lofgren Group in the EPB shared internal beam simultaneously with the California Institute of Technology Group and the Moyer Group.

The University of Washington—U. C. San Diego Group completed their experiment on September 9. A summary of the experimental program for this quarter is shown in Table I.

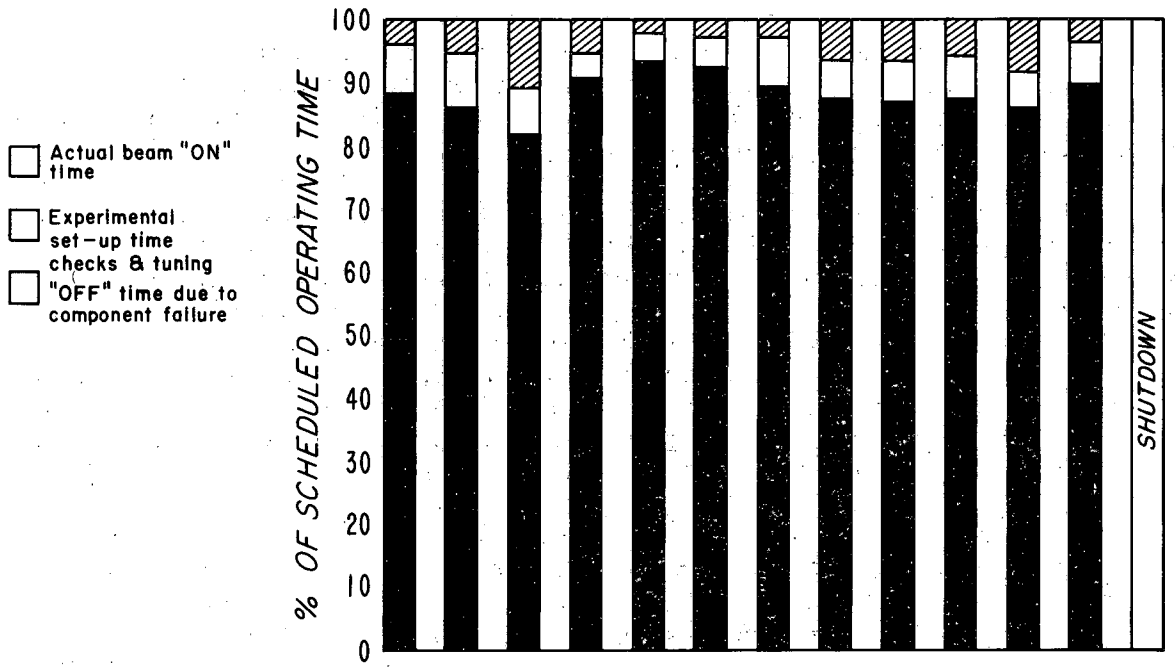


| Week of | 7/2 | 7/9 | 7/16 | 7/23 | 7/30 | 8/6 | 8/13 | 8/20 | 8/27 | 9/3 | 9/10 | 9/17 | 9/24 |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| Crew hours | 144 | 168 | 168 | 168 | 168 | 168 | 168 | 168 | 168 | 144 | 168 | 168 | 168 |
| Turn on & maintenance time (h) | 11 | 13 | 11 | 12 | 11 | 8 | 10 | 10 | 10 | 25 | 10 | 12 | 0 |
| Scheduled operating time (h) | 119 | 136 | 133 | 136 | 134 | 136 | 122 | 130 | 157 | 110 | 137 | 138 | 0 |
| Scheduled Bevatron test time (h) | 14 | 19 | 24 | 20 | 23 | 24 | 36 | 28 | 1 | 9 | 21 | 18 | 0 |
| Scheduled shutdown time (h) | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 168 |
| Holiday | 24 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 0 | 24 | 0 | 0 | 0 |

XBL683-2085

Fig. 1. Bevatron operation record.

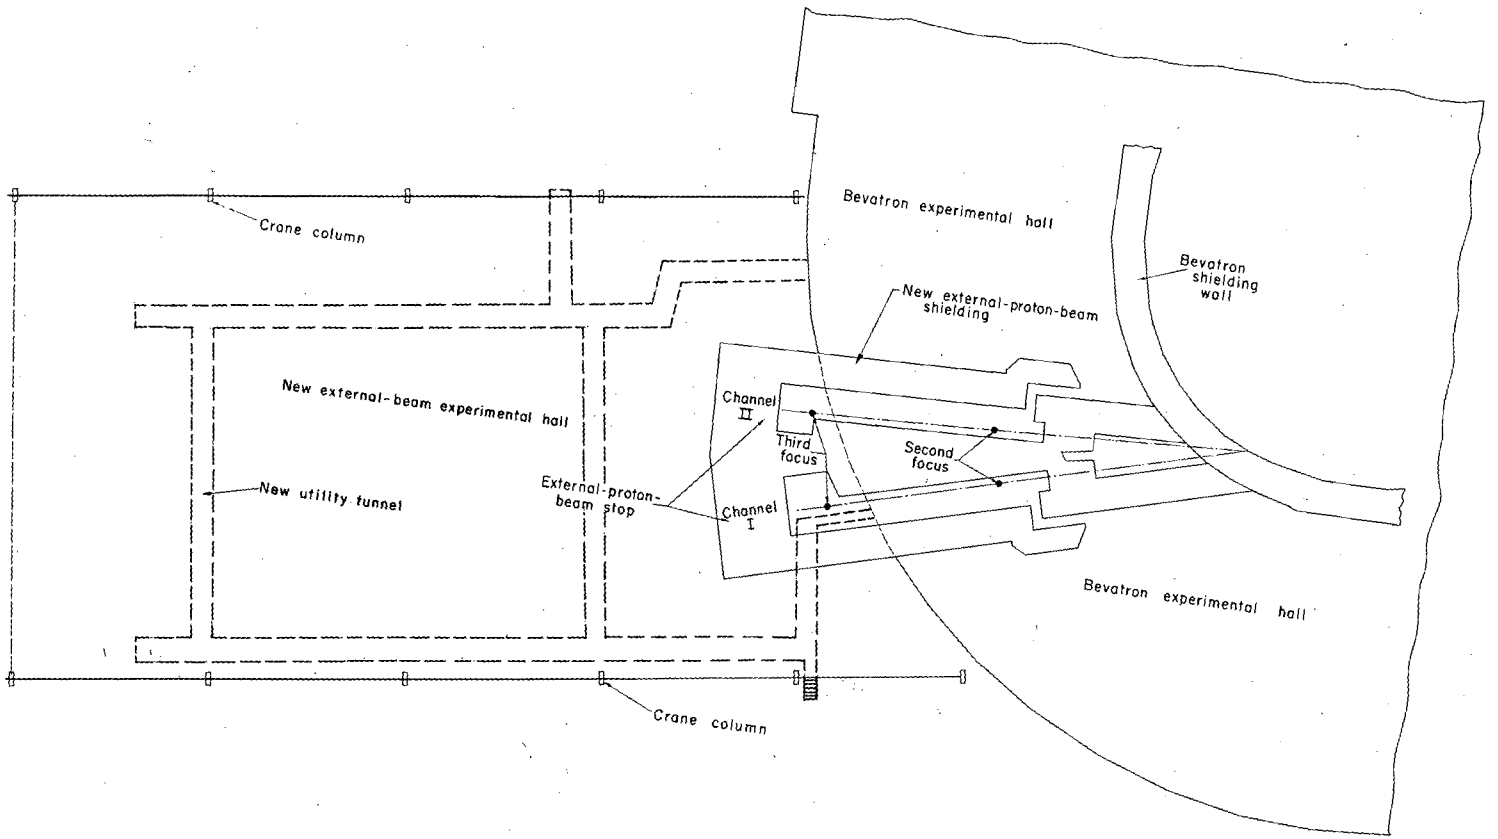


XBL6712-5944

Fig. 2. Utility tunnel layout in new EPB hall.

XBB 676-3301

Fig. 3. New curved-bridge crane installed at north end of craneway of new EPB hall.

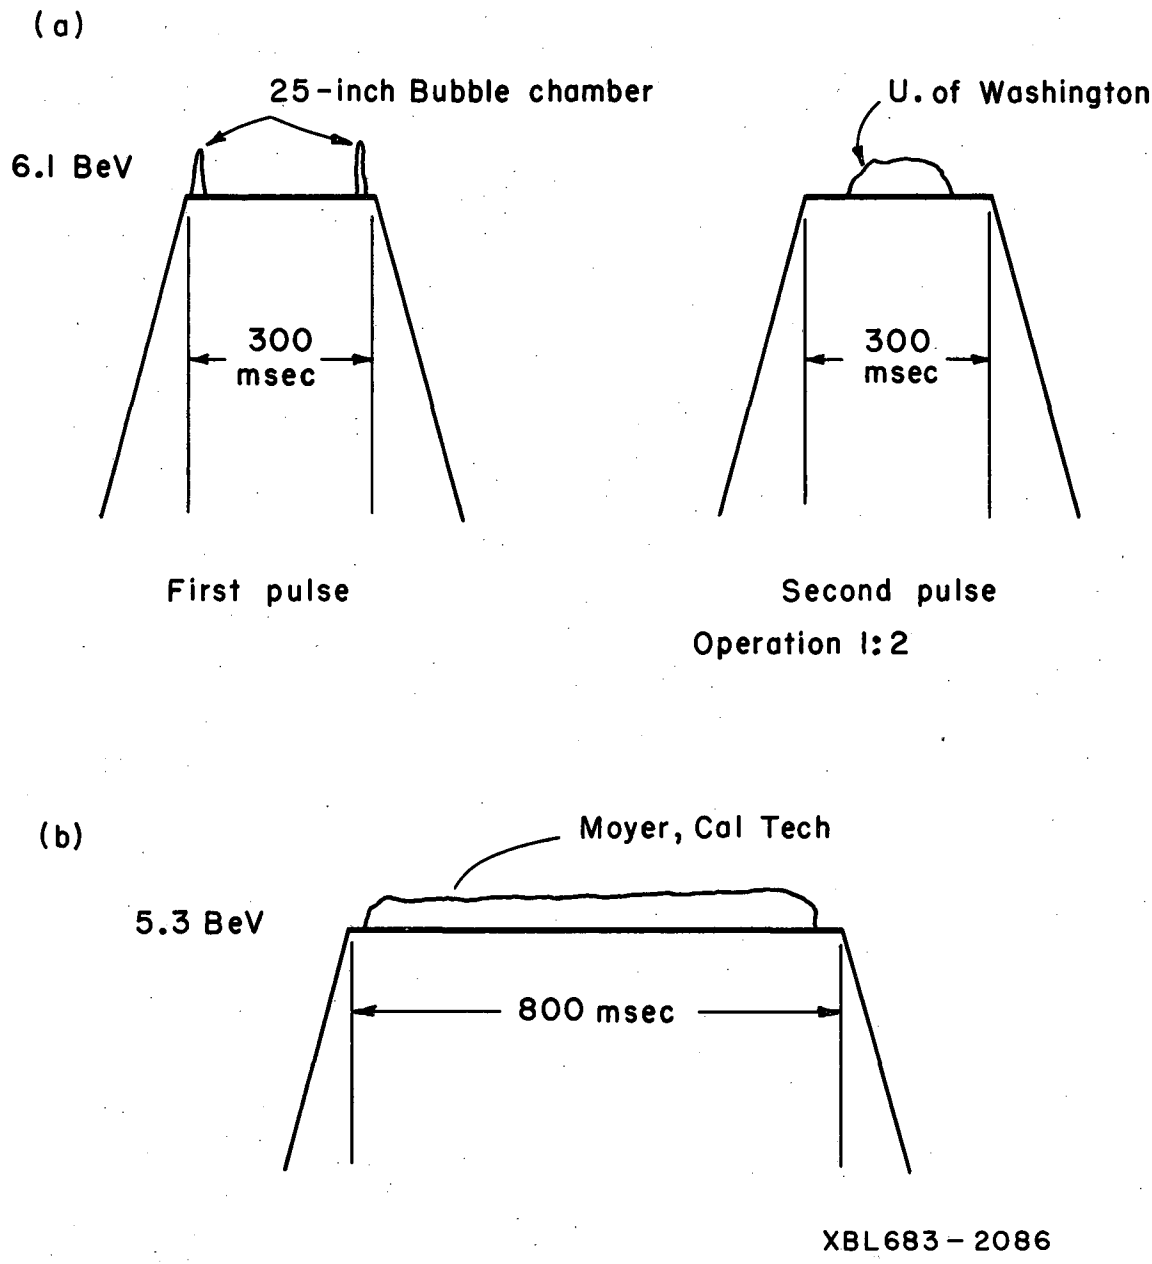


Fig. 4. Bevatron magnet pulsing modes.

Table I. Summary of Bevatron experimental research program, July through September 1967.

| Groups | Dates: Run | Dates: Start | Dates: End | Experiment | Beam Time: This quarter (July-Sept.) 12-Hour periods | Beam Time: This quarter (July-Sept.) Hours | Beam Time: From start of run through September 1967 12-hour periods | Beam Time: From start of run through September 1967 Hours | Pulse schedule | Primary or secondary experiment |
|---|---|---|---|---|---|---|---|---|---|---|
| Internal Groups | | | | | | | | | | |
| Alvarez (Murray) | 39 | 8/5/65 | In progress | $K^0$-$K_2^0$ interference, using the 25-in. bubble chamber | 18 | 131 | 235 | 2435 | 1:1 | P |
| Moyer-Helmholz (Parker) | 47A | 5/19/66 | In progress | Neutral decay rate | 34 | 393 | 125 | 1359 | 1:1 | P |
| | | | | $K_L^0 \rightarrow 2\pi^0$ | 0 | 5 | 66 | 833 | 1:1 | S |
| Lofgren | 67 | 8/28/67 | In progress | $Ke_2$ branching ratio | 2 | 28 | 2 | 28 | 1:1 | P |
| | | 6/7/67 | | 0.5-BeV/c separated $K^+$ beam | 3 | 51 | 7 | 113 | 1:1 | S |
| Trilling-Goldhaber | 75 | 7/25/67 | 8/28/67 | $K^-p$ reactions in 250-MeV/c separated $K^-$ beam, using 25-in. bubble chamber | 43 | 479 | 43 | 479 | 1:2 | P |
| Poskanzer | P-24 | | | Search for $n^x$-neutron multiplets. Nuclear chemistry exposed to Bevatron internal beam | 0 | 2 | | 2 | 1:1 | P |
| External Groups | | | | | | | | | | |
| U. of Washington | 50 | 3/16/66 | 9/9/67 | Magnetic moment of | 0 | 2 | 114 | 1278 | 1:1 | S |
| U. C. San Diego | | 5/20/66 | 9/9/67 | $\Xi^-$ cascade | 5 | 49 | 40 | 430 | 1:1 | P |
| | | 9/10/66 | 9/9/67 | | 70 | 776 | 109 | 1204 | 1:2 | P |
| Calif. Inst. of Technology (Tollestrup) | 80 | 8/31/67 | In progress | Leptonic decay, $K \rightarrow \pi^{\pm}, e^+, \nu$. | 0 | 6 | 0 | 6 | 1:1 | P |
| | | 8/11/67 | | Determination of $\Delta S/\Delta Q$ in 2- to 3-BeV/c $\pi^-$ beam | 10 | 133 | 10 | 133 | 1:1 | S |
| U. of Washington (Davis) | P-12 | 7/21/66 | In progress | Spark chamber tests | 0 | 3 | 20 | 248 | 1:1 | S |
| | | | | for Run No. 54 | 0 | 6 | 38 | 432 | 1:2 | S |

## II. SHUTDOWN

A five-day shutdown was scheduled to start on September 25 for routine maintenance on the main motor generator sets and to relocate an underground 12-kV power line in the EPB Hall construction area. The shutdown started a day early when a generator field pole connection on the east main Bevatron generator failed. The details of the generator repair work are given in Section IV of this report.

There was a short vacuum shutdown to install a new scintillator on the septum and aperture of the resonant extraction magnet. During the original installation of the extraction magnet, a 0.30-in.-thick alumina scintillator had been installed on the septum and across the aperture of the extraction magnet. The alumina did not scintillate well at the beam densities available during extraction studies. A more sensitive scintillator was needed. A zinc sulfide scintillator on 0.003-in. aluminum foil was made. When it was taken into the Bevatron vacuum system to be installed on the magnet, the zinc sulfide came off the aluminum foil. A new zinc sulfide scintillator had to be made, and was installed two days later during a second short vacuum shutdown.

The external proton beam plunging magnets were inspected for wear and radiation damage, and were found in good condition. The graphite septum of the electrostatic inflector had a crack at the output end. A new septum was installed.

The high-voltage column between the Cockcroft-Walton high-voltage supply and the linac was overhauled and nine new insulators installed.

A new water-cooled graphite block was installed as a beam stop between the ion gun and the linac. This replaced an old swing cup that could be placed in the beam. These devices are part of the safety interlock system which stops the beam from the ion source before it goes into the linac.

The remainder of the shutdown work was devoted to routine maintenance of the Bevatron and associated equipment.

## III. BEVATRON DEVELOPMENT AND STUDIES

The machine study periods this quarter were devoted almost exclusively to the problems of resonant extraction of the proton beam. A major part of the time was spent in getting diagnostic equipment built and made operational. Measurements were made of radial and vertical beam dimensions. The radial $\nu$ value was measured as a function of radius. Initial tests were made of the radial growth of the beam, using a perturbation of $\Delta\nu$ equal to -0.02. A gold foil irradiated at the first septum has indicated that all the beam grows to a 5-in. amplitude and has a jump per three turns of about 0.75 in. These results are in satisfactory agreement with the calculations. Tests will continue on resonant extraction.

# IV. MAGNET POWER SUPPLY

Robert Frias

## A. Failure of a Generator Field Pole Connection

At 0120, 24 September 1967, the field of the east generator was relayed off the line, with an indication of a ground on the field excitation power supply. In attempting to locate the problem, we found by visual inspection that the electrical connection between poles No. 3 and No. 4 had parted and that there was a splattering of copper over the adjacent area. An insulation test of the field to ground was taken; it read 500 000 ohms. A megger test was made on the field on the west machines, and showed 80 megohms. Figures 5 and 6 show the broken brazed connections and their location on the generator rotor.

The poles had been installed only 3 months prior to this failure, and carried 1 year's warranty by the Westinghouse Electric Corporation. Westinghouse engineers were called immediately and an investigation of the cause of failure was begun.

The field electrical connections on both machines were cleaned, visually inspected, and "Zyglo" checked. The results of these inspections showed, in addition to the original trouble, cracks in the welds between poles 5 and 6 and between 7 and 8, on the east machine. Cracks were detected on the west machine between poles 3 and 4, 5 and 6, and 7 and 8.

x Rays were taken of numerous connections, and showed a high porosity in most of the brazed joints. The electrical connections (all) were cut open on both machines; this revealed that the brazed connections were poorly bonded. The electrical connections were then cleaned and fitted in preparation for rebrazing. The burned and smoked areas were cleaned and the damaged areas eventually attained an insulation level of more than 200 megohms.

A previously scheduled shutdown for the week of September 25 through 29 to tighten the keys of the generator field poles was started and completed. Preparations were made by Westinghouse to have brazing materials, equipment, and welder here for the week of October 1. A brazing specialist arrived October 1 from the Westinghouse Electric Corporation factory, East Pittsburgh, Pennsylvania, to assist in the brazing technique.

The entire week, October 1 through 7, was utilized in experimenting with different types of brazing materials and methods of brazing. All samples were tested by noting how much strength was required to part the connection. Difficulty was encountered in obtaining a high-quality bond due to the requirements set forth by the Westinghouse factory on the maximum temperature of 250°C at the field coil insulation.

On October 7, after careful consideration of the accumulated data, it was decided to proceed with a technique of brazing on the generators using "Easy Flo" alloy. The connections were made on the west machine and considered to be satisfactory. All brazing was completed by the evening of October 9. The machines were then started and the magnet was pulsed until 0800, 16 October, when they were shut down for normal scheduled maintenance. At this time, all field electrical connections were "Zyglo" inspected and no

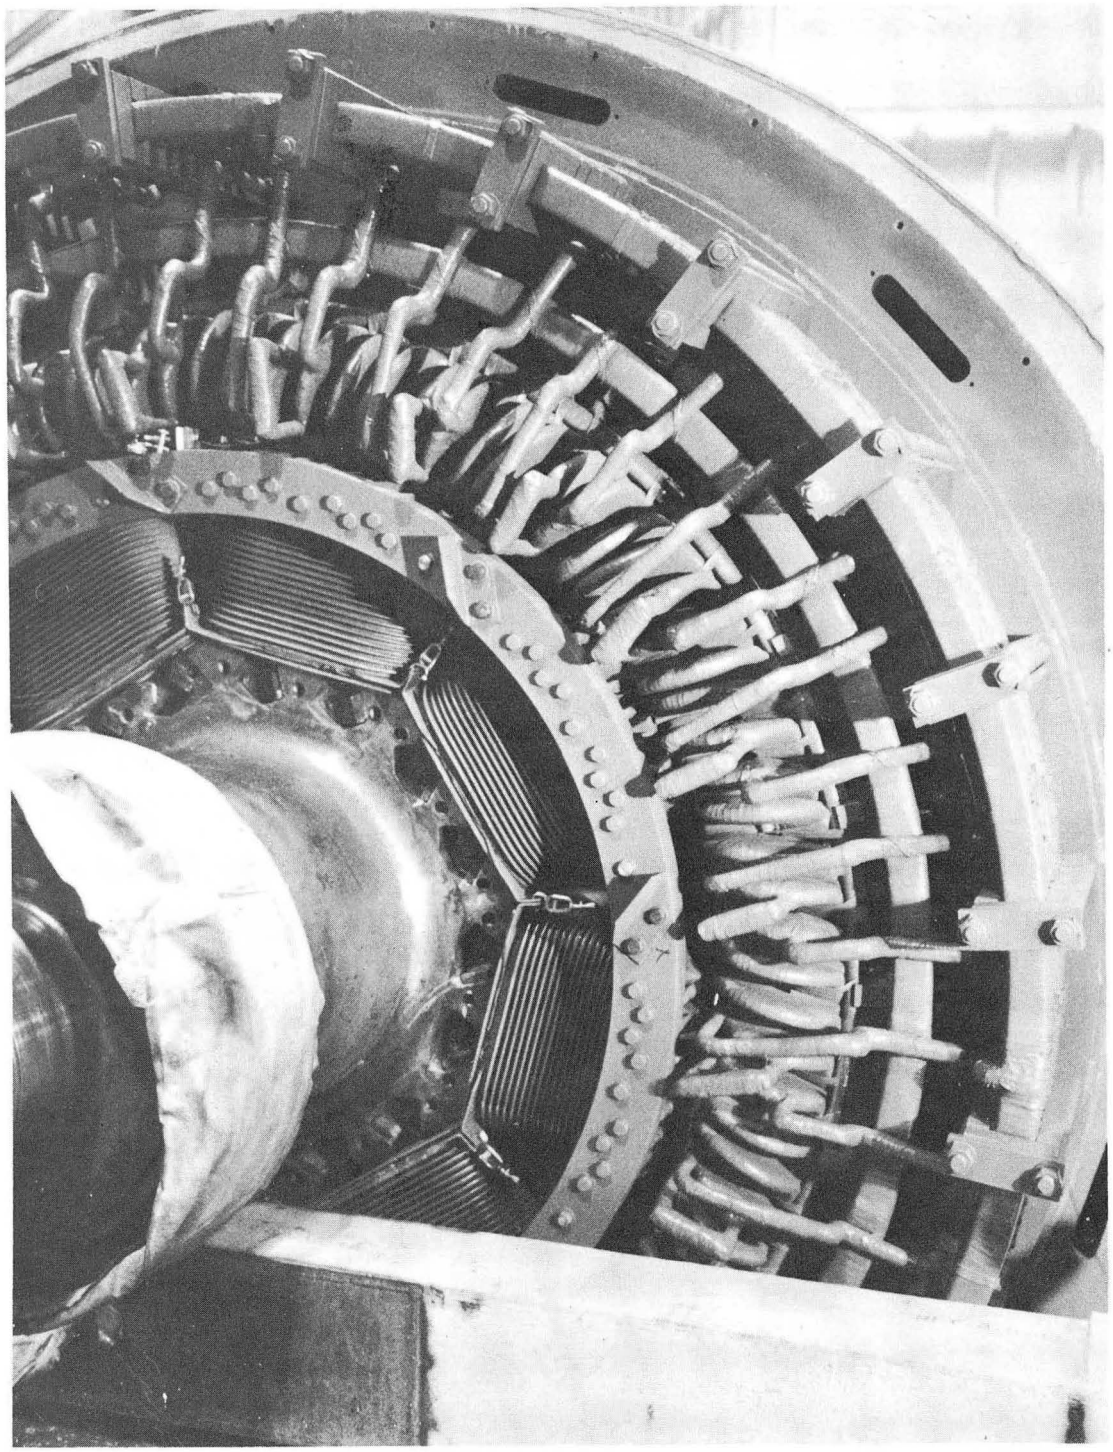

XBB 683-1006

Fig. 5. The location of the brazed coil connection on the 46-MVA generator. The connectors are pointed out by the battery clips.

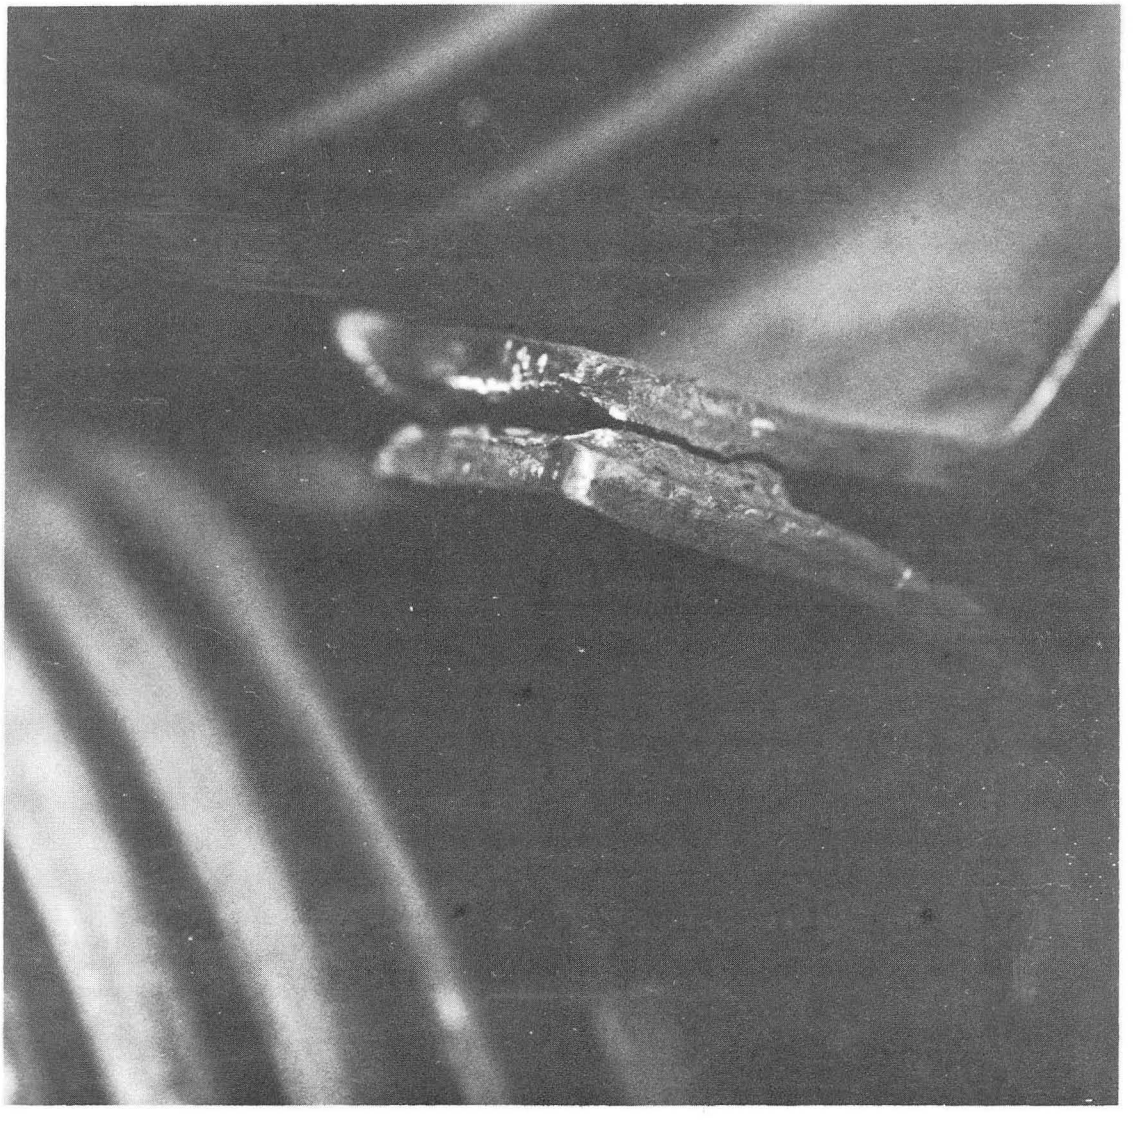

XBB 683-1005

Fig. 6. The break in the pole connection.

faults were found. Voltage drop tests of all connections were made, and considered essentially the same as those made before running. These tests will be continued on a weekly basis until it is assured that the problem has been completely solved.

B. Stability of the Flat-Top Current Slope

Until now, rates of current rise during flat-top have not been critically controlled. Generally, a 50-amp (±5 amp) rise during an 800-msec flat-top has been acceptable tolerance. Developments in resonant extraction of the Bevatron's external beam have called for an increase in pulse-to-pulse stability. Flat-top current slopes of less than 1A for a period of 0.8 sec are now required.

A block diagram of the main control systems in the Bevatron magnet power supply is shown in Fig. 7. The sketch shows three closed-loop systems:

(a) the generator field regulator for ac voltage regulation,
(b) the dI/dt regulator for dc voltage control,
(c) the Kramer regulators for machine speed range control.

Since each of these three loops affects the operational range of the others, it was necessary to establish the proper sequence of adjusting the reference to these regulators. Generally, the following technique is used.

(i) The magnet pulser is set to provide the requested pulse rate and flat-top length. (The Bevatron flat-top period is provided by inverting one power supply while the other is still rectifying.)

(ii) The field regulator is adjusted to insure that each machine provides exactly half of the load. The load is determined by system losses, which, under normal, full-power operation, is 3 MW per machine. With load sharing, repeatable speed-voltage conditions can lead to optimum pulse-to pulse symmetry.

(iii) If variations in speed range exist even though the load is balanced, the Kramer system is adjusted.

(iv) Once the system is stabilized at the required load, the current slope during flat-top is set by adjusting the open-loop firing angle of the grid-controlled ignitrons.

(v) The dI/dt slope control is then switched "on" and the system regulates for a constant B-dot value during the flat-top. This closed-loop control is provided by changing the firing angle of the inverting ignitrons.

An analysis of the B-dot loop output shows that with slopes of from one to two A the pulse-to-pulse repeatability is good. When the tolerance required is less than 1 A, small drifts are still encountered. Development is still under way to reduce these instabilities.

During this development period the setup time required to run the "zero B-dot" mode has been reduced from as long as 1 hour to approximately 2 min.

C. Magnet Pulsing Record

This record is shown in Table II.

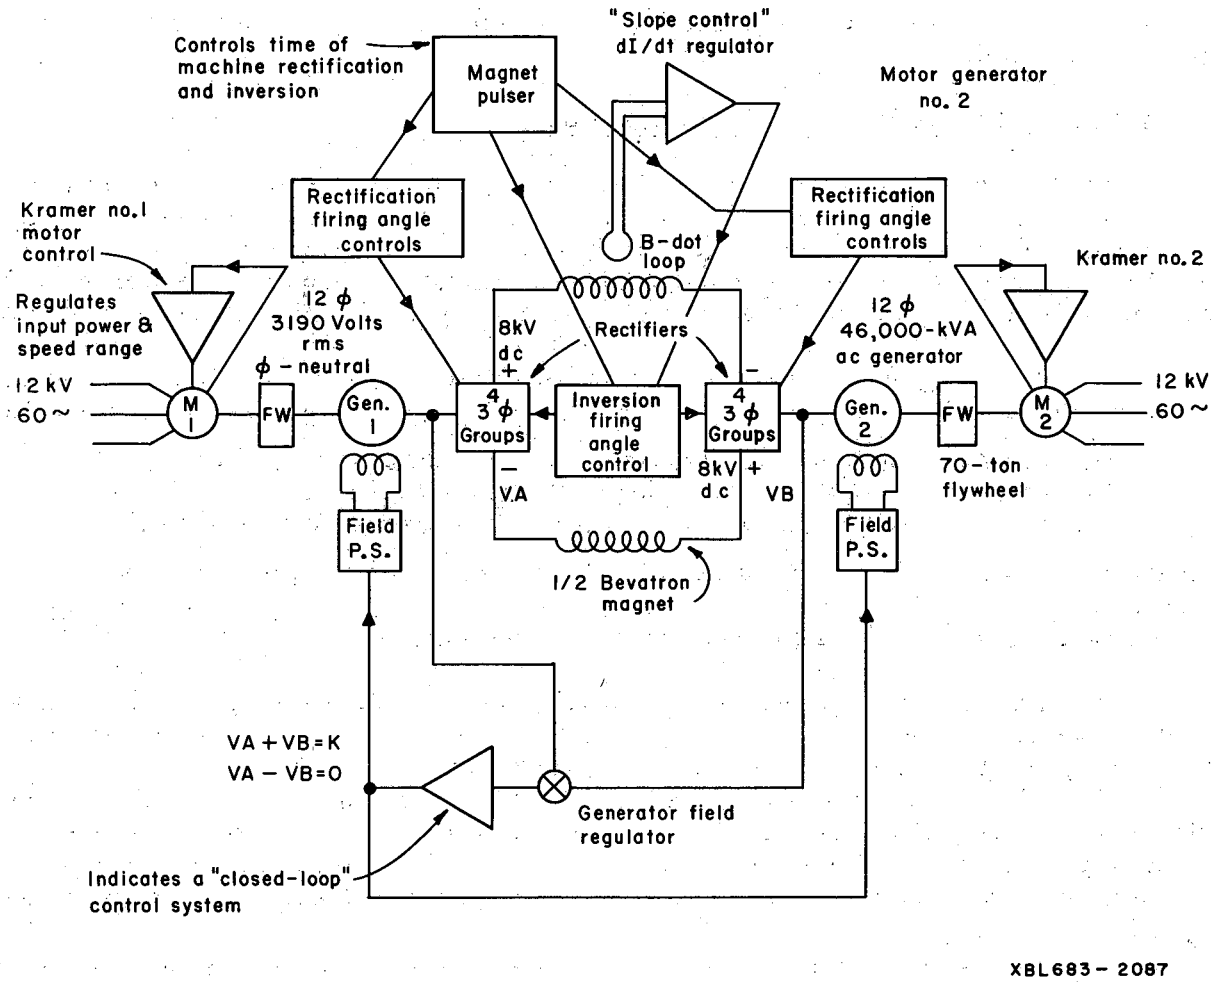


Fig. 7. Bevatron power supply control systems.

Table II. Bevatron motor generator set monthly fault report.

| 1967 | 4 to 6 pulses/min | | | | | | | 7 to 8.7 pulses/min | | | | | | | 9.3 to 17 pulses/min | | | | | | | Total | | | | |
|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|---|
| | 1.5 to 6.9 kA | | | | 7.0 to 9 kA | | | 1.5 to 6.9 kA | | | 7.0 to 9 kA | | | | 1.5 to 6.9 kA | | | 7.0 to 9 kA | | | | | | | | |
| | Pulses | Faults 14 | Faults 26 | P/F | Pulses | Faults 14 | Faults 26 | P/F | Pulses | Faults 14 | Faults 26 | P/F | Pulses | Faults 14 | Faults 26 | P/F | Pulses | Faults 14 | Faults 26 | P/F | Pulses | Faults 14 | Faults 26 | P/F | Total | Arc backs 14 | Arc through 26 | P/F | Ignitrons replaced |
| Jan. | | | | | | | | | | | | | | | | | | | | | | | | | | | | | No pulsing; pole replacement |
| Feb. | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Mar. | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| April | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| May | 1,202 | 0 | 7 | 171 | | | | | | | | | | | | | | | | | | | | | | 0 | 7 | 172 | Over-speed test |
| June | 1,660 | 0 | 0 | ∞ | | | | | 130,221 | 1 | 10 | 11,838 | 48,831 | 3 | 5 | 6,104 | 117,334 | 1 | 2 | 39,111 | 9,662 | 1 | 1 | 4,831 | 307,708 | 6 | 18 | 12,821 | |
| July | | | | | | | | | | | | | 11,281 | 0 | 0 | ∞ | 92,033 | 3 | 8 | 836 | 243,712 | 5 | 17 | 11,079 | 347,026 | 8 | 25 | 10,515 | |
| Aug. | | | | | | | | | | | | | 3,942 | 0 | 0 | ∞ | 141,360 | 3 | 17 | 7,068 | 245,219 | 4 | 12 | 15,300 | 390,521 | 7 | 29 | 10,847 | |
| Sept. | | | | | | | | | 7,182 | 1 | 0 | 7,182 | 15,998 | 1 | 0 | 15,998 | | 8 | 6 | 11,940 | 77,123 | 6 | 2 | 9,641 | 267,551 | 16 | 8 | 11,147 | |
| Oct. | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Nov. | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |
| Dec. | | | | | | | | | | | | | | | | | | | | | | | | | | | | | |

## STAFF

| | |
|---|---|
| E. J. Lofgren | Bevatron Group Leader |
| W. A. Wenzel | Alternate Group Leader |
| Walter D. Hartsough | In charge of Bevatron Operations |
| Kenneth C. Crebbin<br>Fred H. G. Lothrop<br>Wendell Olson | Operation supervisors |
| William Everette | Radiation control |
| Duward S. Cagle<br>Frank W. Correll<br>Robert G. Gisser<br>William H. Kendall | Operating crew supervisors |
| G. Stanley Boyle<br>Robert W. Brokloff<br>Ashton H. Brown<br>Gary M. Byer<br>Donald N. Cowles<br>James R. Guggemos<br>Charles H. Hitchen<br>Arthur K. Ikuma<br>Robert M. Miller<br>Joseph F. Smith<br>Harvey K. Syversrud<br>Marsh M. Tekawa<br>John E. Tommaney<br>Stanley T. Watts | Bevatron operators |
| Robert W. Allison, Jr.<br>Yves M. Baconnier<br>Warren W. Chupp<br>Kenneth C. Crebbin<br>Tom Elioff<br>Robert Force<br>Fred H. G. Lothrop<br>Donald Milberger<br>Robert Richter<br>Glenn White<br>William A. Wenzel<br>Emery Zajec | Development and support |
| Edward Hartwig<br>Robert Force | In charge of Electrical Engineering Group |
| Marion Jones | In charge of Electrical Coordination Group |
| Kenow Lou<br>Cedric Larson | In charge of Mechanical Engineering Group |
| Harold Vogel | In charge of Motor Generator Group |

This report was prepared as an account of Government sponsored work. Neither the United States, nor the Commission, nor any person acting on behalf of the Commission:

A. Makes any warranty or representation, expressed or implied, with respect to the accuracy, completeness, or usefulness of the information contained in this report, or that the use of any information, apparatus, method, or process disclosed in this report may not infringe privately owned rights; or

B. Assumes any liabilities with respect to the use of, or for damages resulting from the use of any information, apparatus, method, or process disclosed in this report.

As used in the above, "person acting on behalf of the Commission" includes any employee or contractor of the Commission, or employee of such contractor, to the extent that such employee or contractor of the Commission, or employee of such contractor prepares, disseminates, or provides access to, any information pursuant to his employment or contract with the Commission, or his employment with such contractor.
